COS30049 – Computing Technology Innovation Project

Week 2 - Scope, Time, and Project Communication Management

Ricky Dong
rdong@swin.edu.au

Acknowledgement of Country

We respectfully acknowledge the Wurundjeri People of the Kulin Nation, who are the Traditional Owners of the land on which Swinburne's Australian campuses are located in Melbourne's east and outer-east, and pay our respect to their Elders past, present and emerging.

We are honoured to recognise our connection to Wurundjeri Country, history, culture, and spirituality through these locations, and strive to ensure that we operate in a manner that respects and honours the Elders and Ancestors of these lands.

We also respectfully acknowledge Swinburne's Aboriginal and Torres Strait Islander staff, students, alumni, partners and visitors.

We also acknowledge and respect the Traditional Owners of lands across Australia, their Elders, Ancestors, cultures, and heritage, and recognise the continuing sovereignties of all Aboriginal and Torres Strait Islander Nations.



Beneficial Randomness

Fuzz Testing (Fuzzing)

- Random Testing
- Generate plenty of inputs to test the program
- AFL++ is still the state-of-the-arts
- Adaptive random testing (TY Chen invented this idea)

"Tibo" (Thibault Sottiaux)

- the Head of Core Products and OpenAI Codex
- "Father of the Reset" or "Saint Tibo: Giver of Tokens."

Let me have a look what I can do for you ...

- Random benefits is up to your feedbacks and performance

SWINBURNE UNIVERSITY OF TECHNOLOGY

Objectives of Today

Scope Management

- **Define Scope**
- **Create WBS**
- **Scope Validate / Control**

Time Management

- **Schedule management**
- **Activities management**

Communication Management

- **Minutes of Meeting**

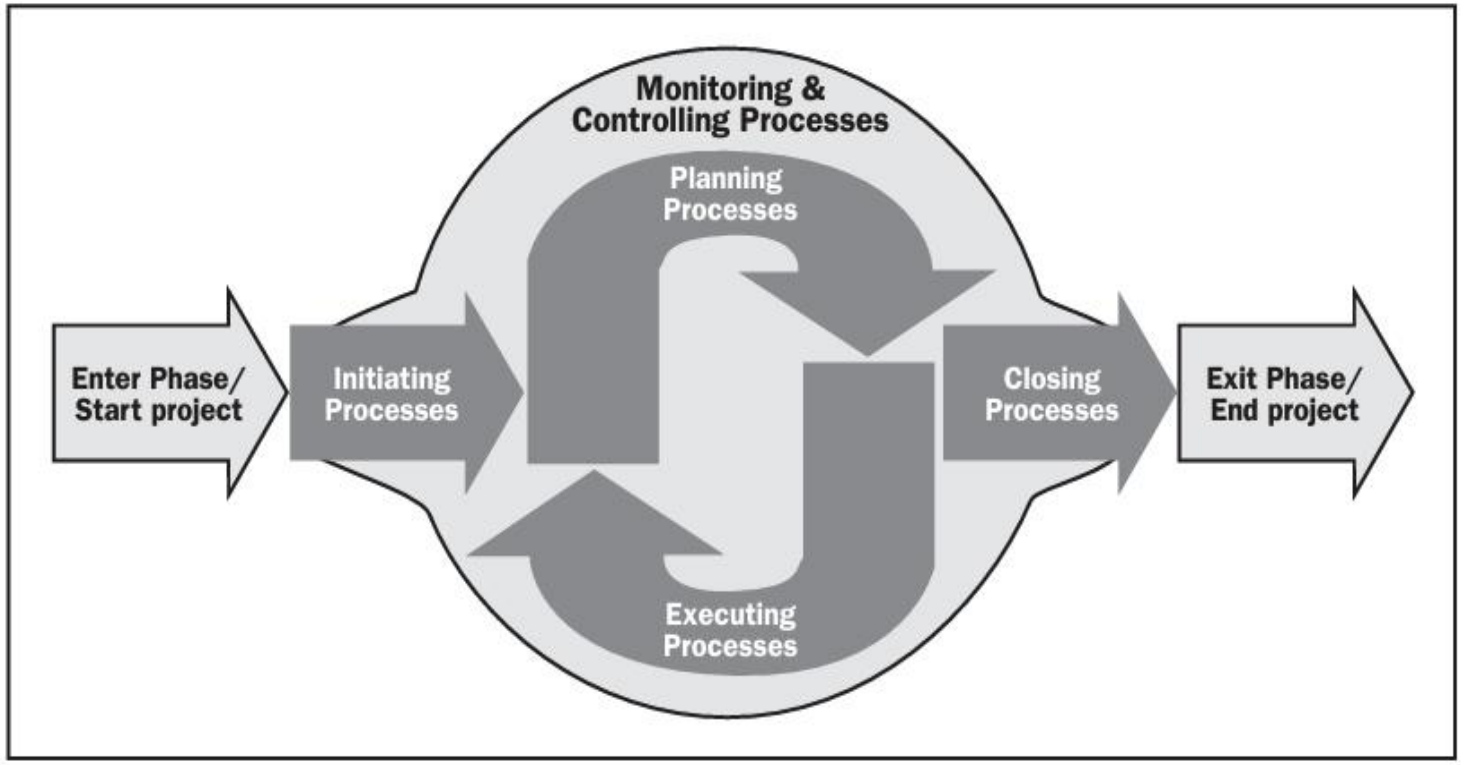


Image from [Reddit]

SWINBURNE UNIVERSITY OF TECHNOLOGY

Project lifecycle

1. Selection and Initiation
2. **Planning**
3. Execution
4. Monitoring & Controlling
5. Closing



Project Management Process,

Project Management Institute, 2001, p.40

SWINBURNE UNIVERSITY OF TECHNOLOGY

Importance of Scope and Time Management

Overview of Project Constraints:

Projects are bound by scope, time, cost, and quality constraints. Balancing these constraints is crucial to project success

Impact on Project Success:

- Effective management ensures the project meets its objectives and is delivered on time and within budget.
- Failure to manage scope and time can lead to project overruns, missed deadlines, and increased costs.

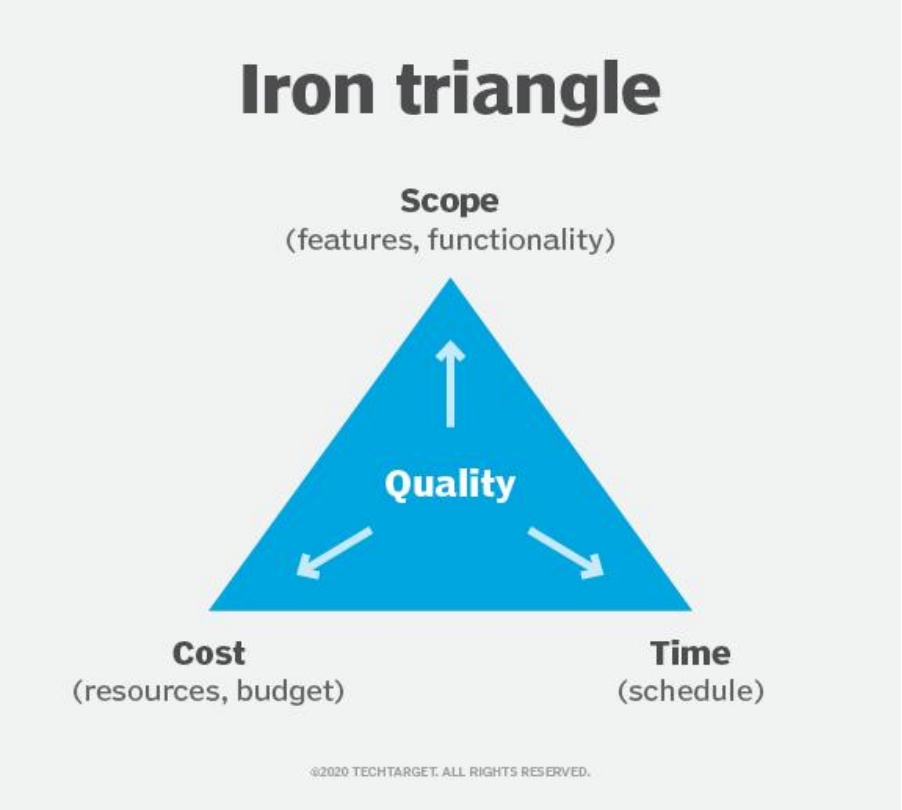


Image from [Project Constains by Paul Kirvan]

Case Study

Emphasizing the Importance of Scope and Time Management Plan


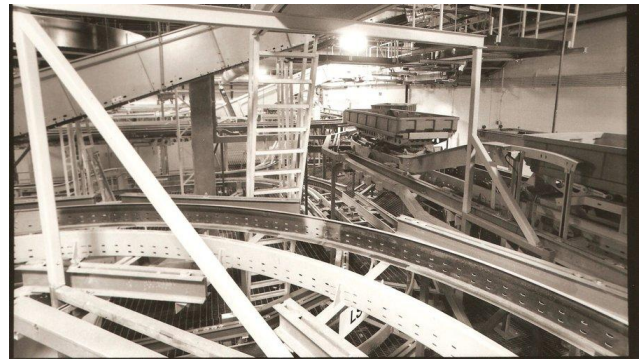


Image Source: [Biz Journals]

Backgroud: A software development company, TechSolutions, was contracted to develop a custom customer relationship management (CRM) system for a mid-sized retail business, RetailMasters. The project was estimated to take six months to complete with a budget of $500,000.

Initial Project Scope:

- Develop a web-based CRM system.
- Key features: customer database, sales tracking, customer support ticketing, and reporting.
- Integration with existing e-commerce platform.
- Training for RetailMasters' staff.



Time Management Plan:

- **Month 1**: Requirements gathering and initial design.
- **Month 2-3**: Development of core features (customer database, sales tracking).
- **Month 4-5:…..**
- **Month 6**: Testing, bug fixing, and staff training.


Challenges Faced:

1. **Scope Creep**:
- As development progressed, RetailMasters requested additional features like a mobile app, advanced analytics, and a loyalty program module.
- These requests were not part of the original project scope and were added without formal approval or adjustments to the time and cost estimates.

2. **Poor Time Management**:
- The project team did not adhere to the initial time management plan.
- Delays in the requirements gathering phase impacted the development schedule.
- Inadequate resource allocation and lack of regular progress tracking further compounded the delays.

SWINBURNE UNIVERSITY OF TECHNOLOGY

Scope Management

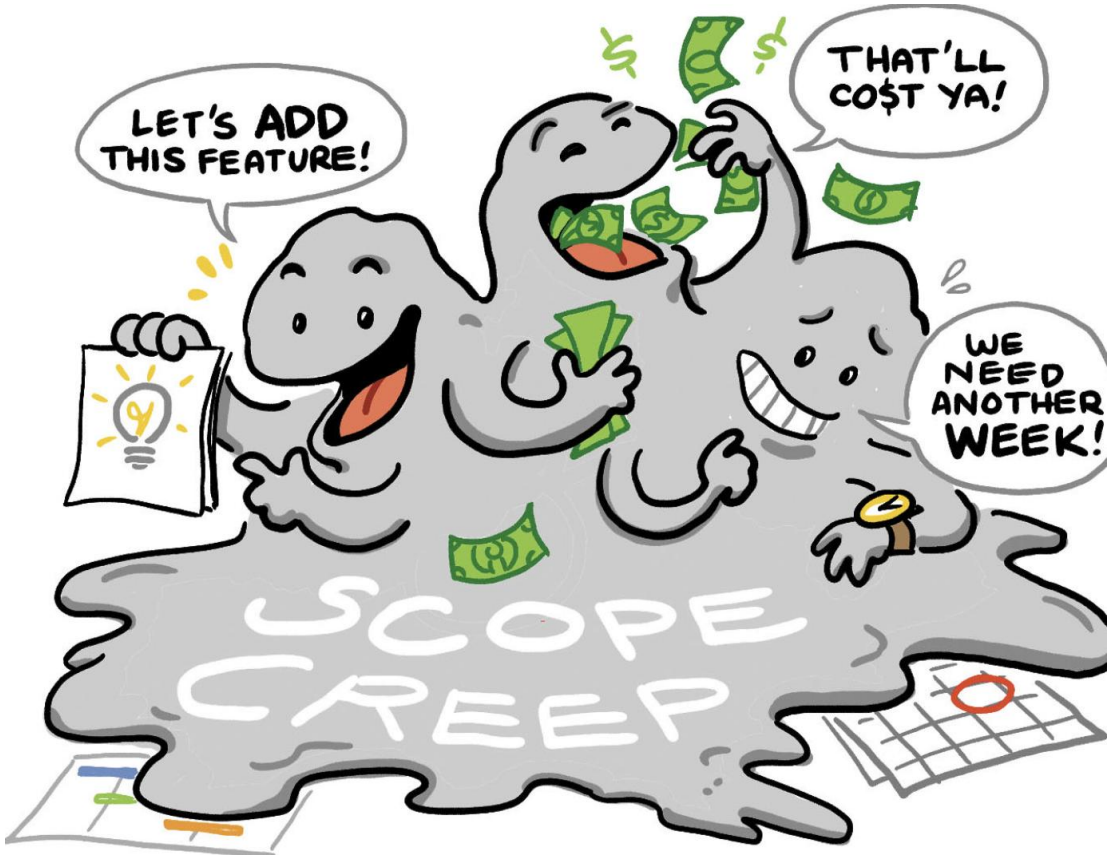

(Source)

SWINBURNE UNIVERSITY OF TECHNOLOGY

Scope Management - Definition

Definition:
Scope Management involves defining and controlling what is included and excluded from a project.

Key activities include:

- Defining Project Scope: Determining the boundaries and deliverables of the project.
- Creating the Work Breakdown Structure (WBS): Breaking down the project into smaller, manageable components.
- Verifying the Scope: Ensuring project deliverables meet required standards and gaining stakeholder acceptance.
- Controlling the Scope: Monitoring project progress and managing changes to the scope baseline.

Purpose:

- **Ensures All Project Requirements Are Met**: Provides a clear understanding of what needs to be delivered, ensuring that all project objectives are achieved.
- **Prevents Scope Creep**: Controls changes to the project scope, preventing the project from expanding beyond its original objectives.
- **Improves Stakeholder Communication**: Ensures that all stakeholders have a common understanding of the project scope, leading to better collaboration and communication.

SWIN BUR NE SWINBURNE UNIVERSITY OF TECHNOLOGY

Scope Management Processes

Processes:

1. Plan Scope Management
2. Collect Requirements
3. Define Scope
4. Create WBS (Work Breakdown Structure)
5. Validate Scope
6. Control Scope

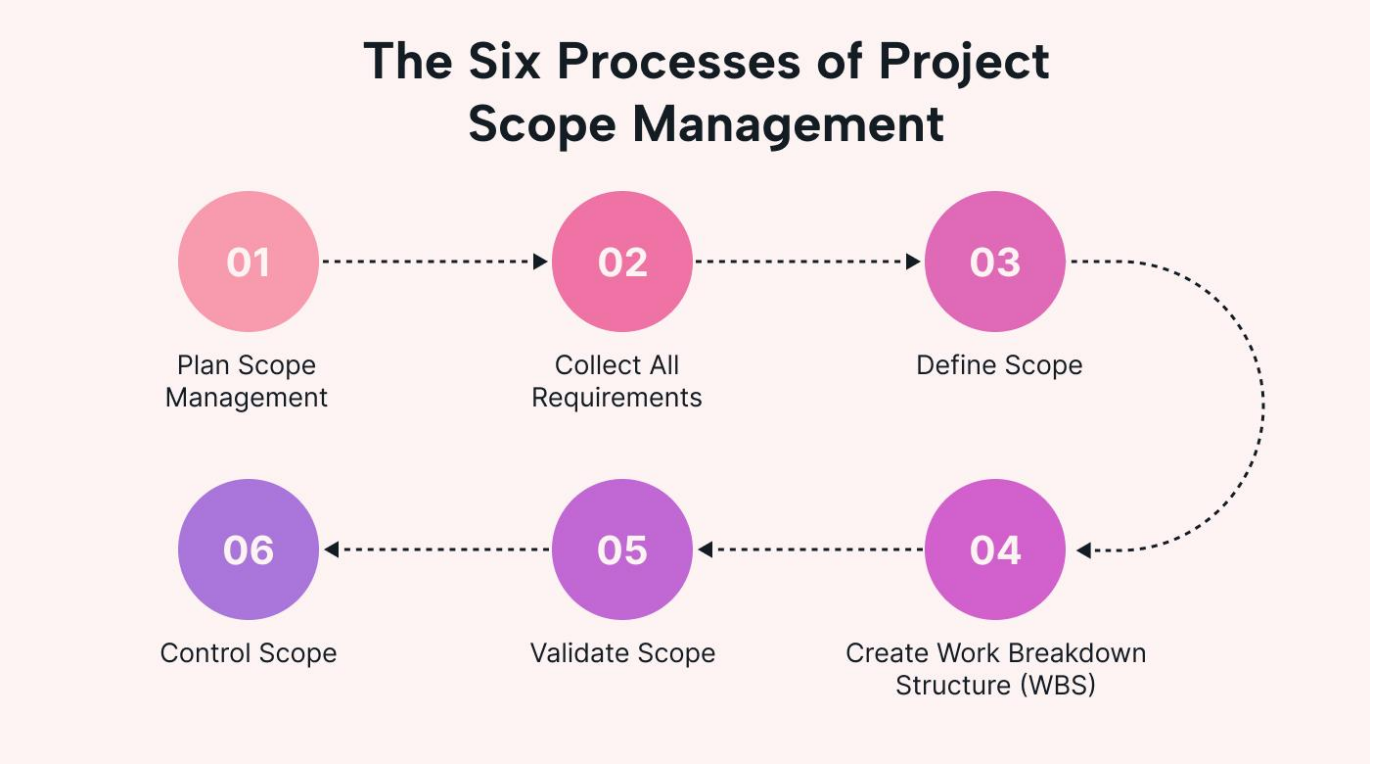


Image Source: [Project Scope Management: What It Is and How to Master It Motion Blog]

What are these processes for?

Case Study

Developing an E-Commerce Website



This Photo by Unknown Author is licensed under CC BY-NC-ND

Backgroud: You are part of a project team tasked with developing a comprehensive e-commerce website for a retail company. The goal is to enhance the company's online presence and provide a seamless shopping experience for customers. The project requires detailed planning, execution, and monitoring to ensure its success.

Task:

1. Define Scope: Clearly outline the project's scope by creating a detailed project scope statement. This document should specify the functionalities of the website, the project's timeline, and budget constraints.

2. Work Breakdown Structure (WBS): Develop a Work Breakdown Structure (WBS) to decompose the project into smaller, manageable components. The WBS should include all major deliverables and tasks necessary for project completion.

3. WBS Dictionary: Create a WBS Dictionary that provides detailed information about each component in the WBS. Include descriptions, responsibilities, deliverables, and criteria for completion for each task.

4. Gantt Chart: Develop a Gantt Chart to visually represent the project schedule. The Gantt Chart should illustrate the timeline for each task, including start and end dates, dependencies, and milestones.

5. Meeting Minutes: Document the key points and decisions made during a project planning meeting. The meeting minutes should capture discussions on the project scope, WBS, WBS Dictionary, and Gantt Chart.

SWINBURNE UNIVERSITY OF TECHNOLOGY

01 - Plan Scope Management (A1)

We need a plan not only managing the project, but also for managing the scope of the project.

Definition:
Plan Scope Management is the process of creating a scope management plan that documents how the project scope will be defined, validated, and controlled throughout the project lifecycle.

Importance:

Provides guidance on how the project scope will be defined, documented, and managed.

Key Components:

- **Inputs:** Project charter, project management plan
- **Tools & Techniques:** Expert judgment, data analysis
- **Outputs:** Scope management plan, requirements management plan

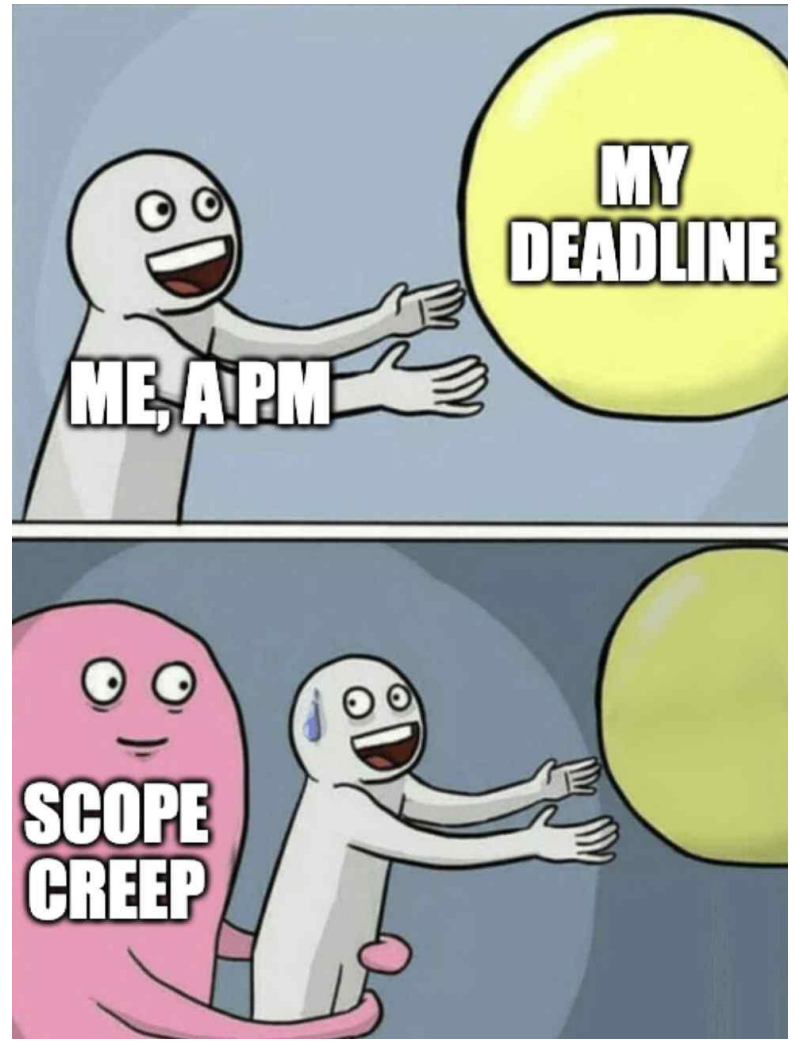


Image Source: [Project Management Memes Visor Blog]

02 - Collect Requirements (A1)

Definition:
Collect Requirements is a process within scope management that involves determining, documenting, and managing the needs and requirements of the project stakeholders.

Importance:
Ensures that all stakeholder needs and expectations are captured and addressed, leading to a project that meets its objectives.

Techniques:
Interviews, Surveys, Focus Groups, Brainstorming, Observation

Documenting Requirements:

- **Requirements Documentation**: Detailed descriptions of how individual requirements meet the business need for the project.
- **Requirements Traceability Matrix**: A grid that links requirements to their origin and traces them throughout the project lifecycle.

Project Name		Date	
Project Number		Document Number	
Project Manager		Project Owner/Client	

ID Number	Date Received	Source	Requirement Name and Description	Assigned To	Acceptance Criteria	Tested By and Date	Accepted By and Date

How to define requirements? (review from week 1)


The following processing ideas can be used when defining requirements and producing a project proposal

In your assignment 1, you need to list functional and non-funcitonal requirements (collected from your proposed customers/stakeholders)

- Functional requirements: What the system must do. Features, specific behaviors, and tasks the system must execute (e.g., users can log in via email).
- Non-functional requirements: How the system must perform. Quality attributes like speed, security, reliability, and usability (e.g., pages load in under 2 seconds).

Image from CRVS Digitisation Guidebook

Define the context and objectives of the project: Understand the origin and objectives of the project, and identify why the project was initiated and what it is expected to achieve.

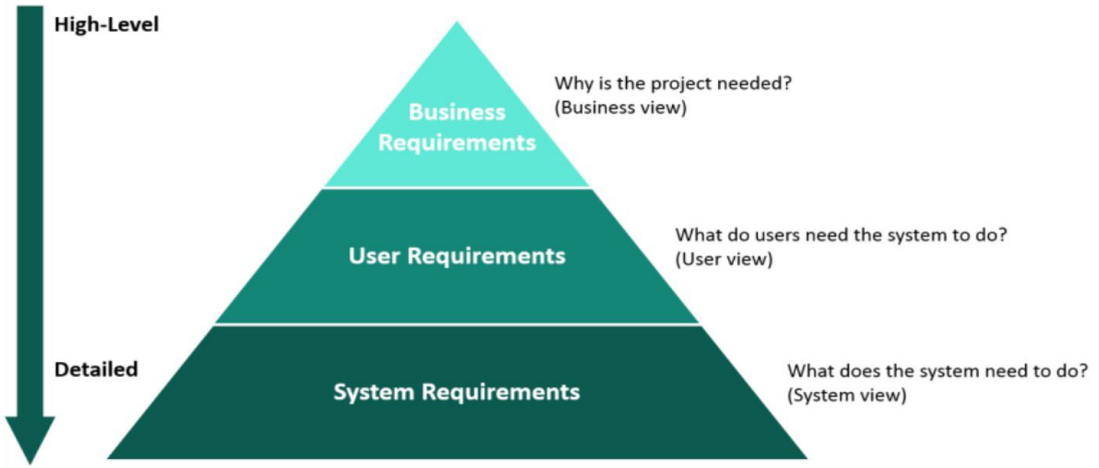


Requirements Hierachy

03 - Define Scope (A1)

Definition:
Define Scope is the process of developing a detailed description of the project and product. It includes defining the project boundaries, deliverables, assumptions, and constraints to ensure clarity for all stakeholders.

Project Scope Statement:
- Detailed Description: Provides a comprehensive outline of the project scope.
- Deliverables: Specifies the outputs or products that will be delivered by the project.
- Assumptions: Lists any assumptions made during the project planning.
- Constraints: Identifies any limitations or restrictions that may impact the project.

Importance:
- Ensures all stakeholders have a common understanding of the project scope.
- Helps in managing stakeholder expectations and preventing scope creep.
- Provides a clear framework for decision-making and project execution.

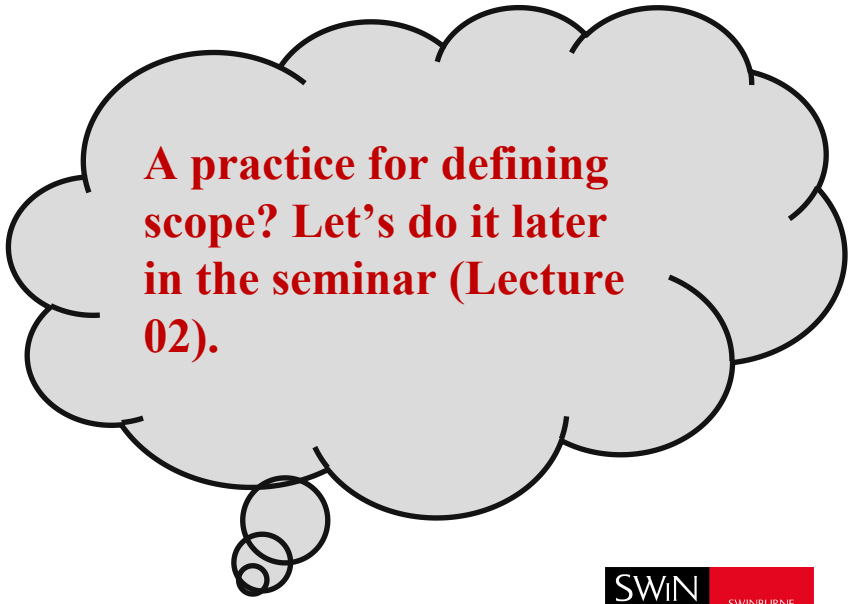

SWINBURNE UNIVERSITY OF TECHNOLOGY

How to Define Scope - Example

Developing an E-Commerce Website

1. Project Scope Statement: Develop a detailed document specifying the e-commerce website functionalities, timeline, and budget constraints. Ensure all aspects from design to deployment are covered.

2. Deliverables: Key deliverables include the website design, user registration system, shopping cart functionality, payment gateway integration, and user feedback system.

3. Assumptions: Assumptions include availability of necessary resources, client's timely feedback, and stable internet access for development and testing.

4. Constraints: We identify constraints, such as budget limits, technology stack restrictions, and regulatory compliance requirements.

SWINBURNE UNIVERSITY OF TECHNOLOGY

04 - Create WBS (A1)

Definition:


Work Breakdown Structure (WBS) is a hierarchical decomposition of the total scope of work to accomplish the project objectives and create the deliverables.

Purpose:

The WBS organizes and defines the total scope of the project by breaking it down into smaller, more manageable components.

Steps to Create a WBS:

- Identify deliverables
- break down into smaller components
- review with stakeholders

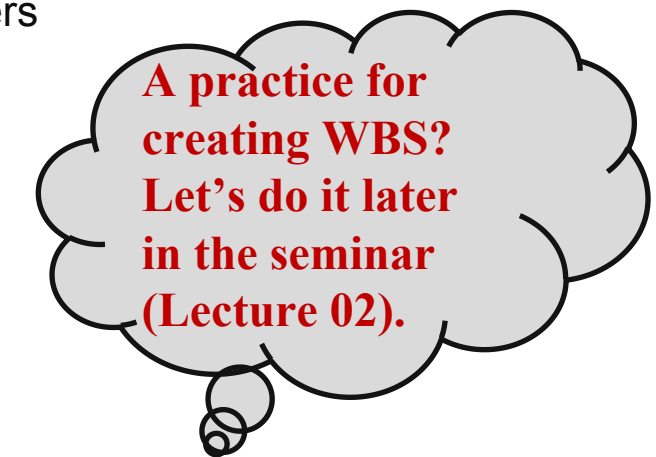



An example of a website project WBS (Source)

Different Approaches of Developing A WBS

Guidelines:
Follow established guidelines from organizations for preparing WBSs.

Analogy approach
Review WBSs from similar projects and tailor them to fit your project's needs.

Top-down approach (A1)
Start with the largest components of the project and break them down into smaller tasks.

Bottom-up approach
Begin with specific tasks and aggregate them into larger work packages.

Mind-mapping approach
Write tasks in a non-linear, branching format and then organize them into a structured WBS.



An example of a website project WBS (Source)

SWINBURNE UNIVERSITY OF TECHNOLOGY

How to Develop a WBS?- Example

Developing an E-Commerce Website

Why Step 3 & 4 are not in our WBS diagram???

Steps to Create a WBS:

1.**Identify Deliverables**: The first step is to determine the major deliverables or outputs of the project. For our example, these are the main phases such as Planning, Implementation, Monitoring and Control, and Deployment.

2. **Decompose Deliverables**: Next, we break down each deliverable into smaller, more manageable components or work packages. For instance, under Implementation, we have tasks like developing the architecture, developing the product database, developing the website, and testing the site.

3. **Assign Responsibilities**: Each work package should be allocated to a specific team or individual who will be accountable for its completion.

4. **Review with Stakeholders**: Collaborating with stakeholders is crucial to ensure the WBS is comprehensive and that nothing is overlooked.

5. **Finalize WBS**: Finally, ensure that the WBS covers the entire project scope and is agreed upon by all stakeholders.


SWINBURNE UNIVERSITY OF TECHNOLOGY

How to develop a WBS?

We will use a top-down approach to establish the structure of a generic WBS.

Level 0: Put the project itself at the top

Level 1: Depending on the method we choose to decompose the deliverables of the project, **Level 1 of the WBS could be called main deliverables, stages, or phases of the project.**

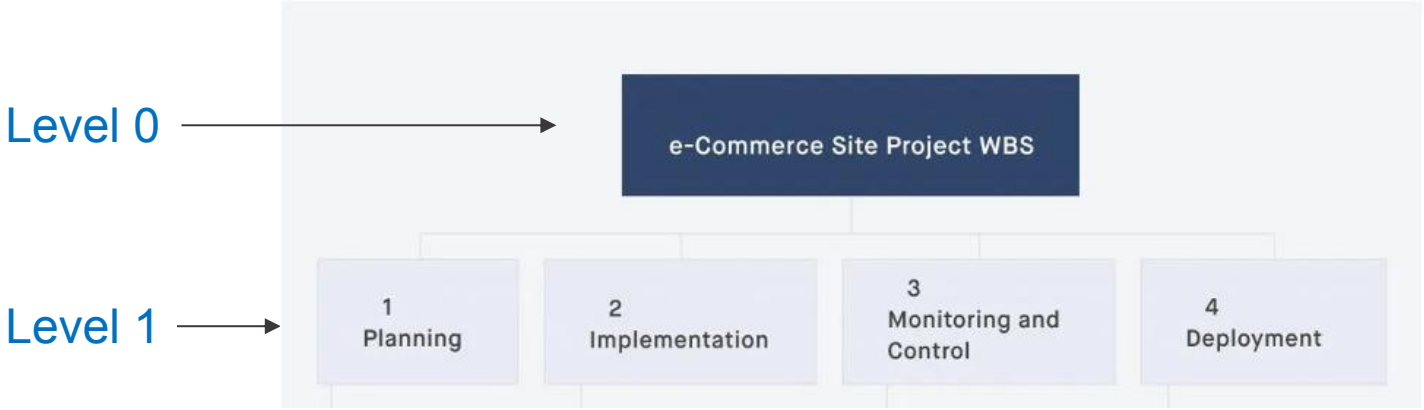

In our example, we use the **Top-Down Approach** to decompose the project deliverables:


It starts with the main project (1.0 e-Commerce Site Project WBS) at the top level which is Level 0, then breaks it down into major phases or stages (1.1 Planning, 1.2 Implementation, 1.3 Monitoring and Control, 1.4 Deployment) at the next level (follows a Waterfall methodology approach.)

SWINBURNE UNIVERSITY OF TECHNOLOGY

How to develop a WBS?

At Level 2, we further decompose each element from Level 1 into more detailed components. These components represent the major deliverables for each element, providing a clearer picture of the specific tasks and activities required to complete each phase of the project.

Level 2 of the WBS provides a detailed breakdown of the tasks needed to complete each phase of the project, offering clear guidance on the specific activities required to achieve the project's objectives. This detailed decomposition helps in better planning, assigning responsibilities, and tracking progress.

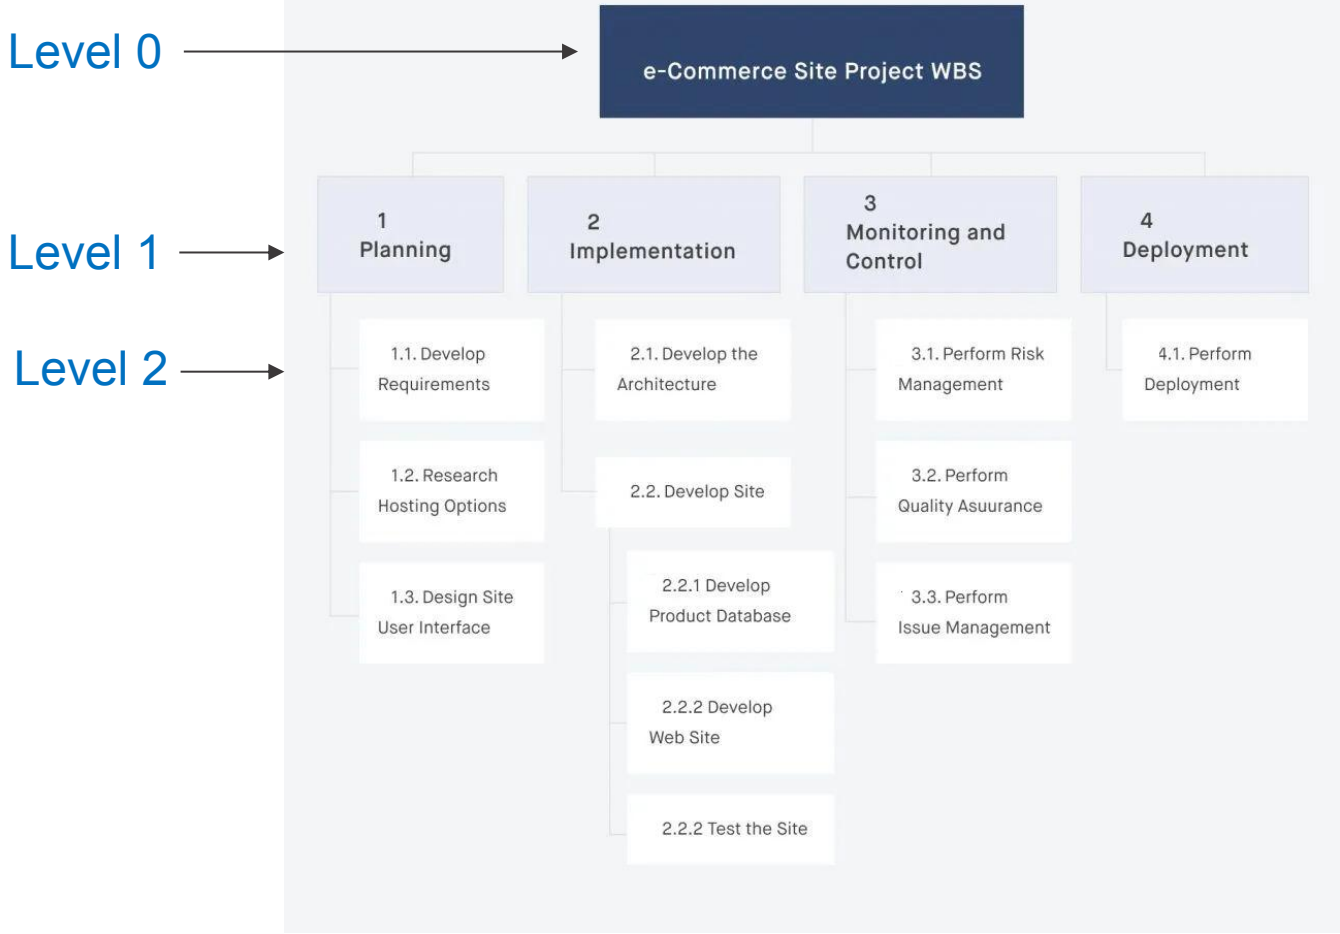


SWINBURNE UNIVERSITY OF TECHNOLOGY

How to develop a WBS?

Depending on the complexity of the project and the level of detail required for effective management, it may be necessary to further break down these components into additional levels, such as Level 3 (developing to level 3 is enough to your A1).

This further decomposition helps ensure that all tasks are clearly defined, manageable, and easily assignable. Each subsequent level provides more granularity, allowing for better planning, resource allocation, and progress tracking.

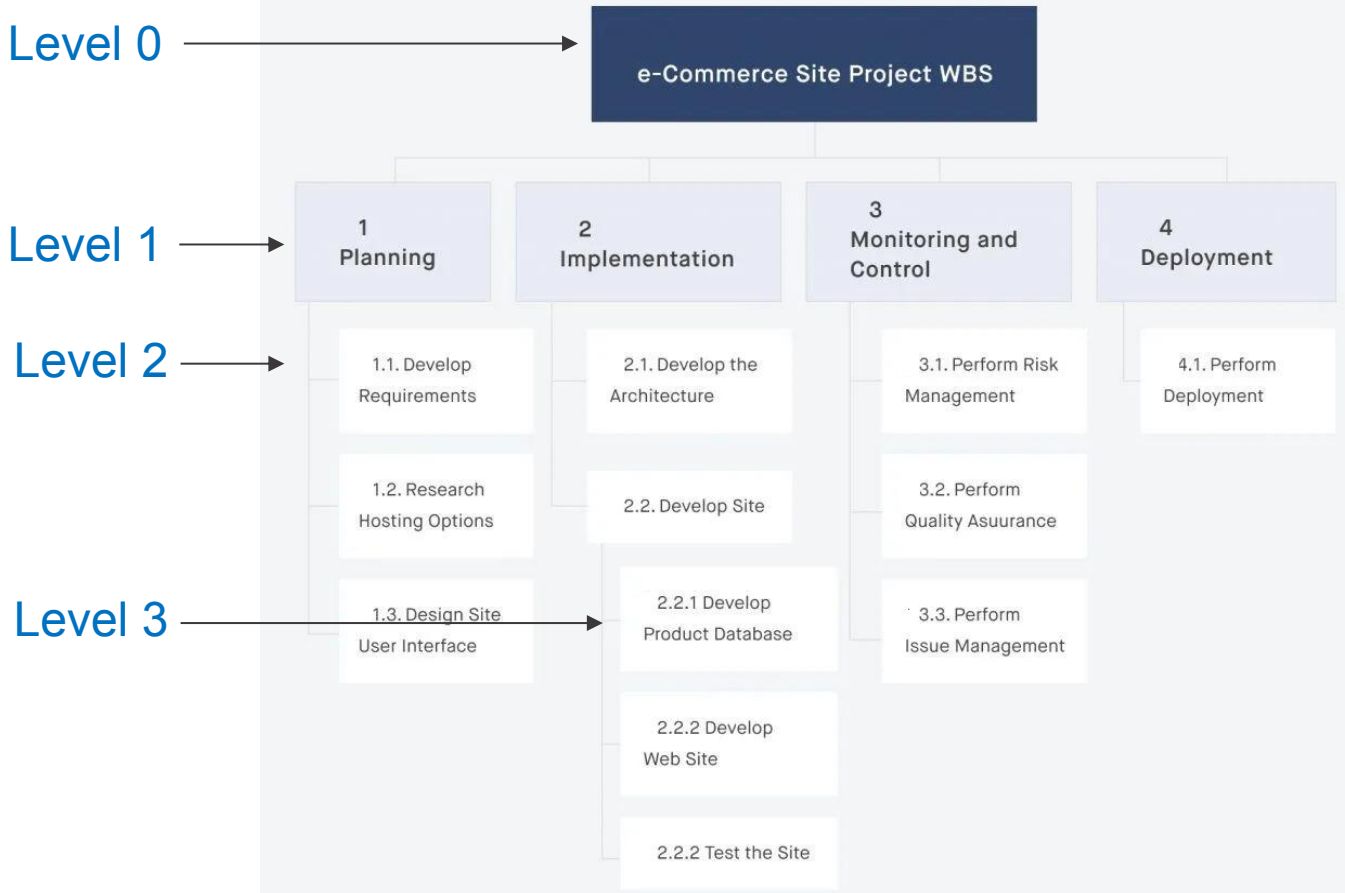

WBS Dictionary (A1)

Definition
A WBS Dictionary is a detailed document that provides comprehensive information about each element in the Work Breakdown Structure (WBS).

Purpose
It clarifies the scope, deliverables, activities, and responsibilities associated with each WBS element.

Components
Typically includes Level, WBS Code, name, Description, Predcecessors, Duration, Resources and cost estimates.

Level	WBS Code	WBS Name	Description	Predecessors	Duration	Resources	Cost
1	1						
2	1.1						
3	1.1.1						
3	1.1.2						
3	1.1.3						

SWINBURNE UNIVERSITY OF TECHNOLOGY

WBS Dictionary - Example

Level	WBS Code	Task Name	Description	Responsible	Start Date	End Date
...	...	...	...	...	...	...
2	1.1	Develop Requirements	Gather and document stakeholder requirements.	Business Analyst	1/1/2024	4/1/2024
2	1.2	Research Hosting Options	Research and select a hosting provider.	IT Specialist	5/1/2024	9/1/2024
2	1.3	Design Site User Interface	Design the layout and user interface of the website.	UI/UX Designer	10/1/2024	14/1/2024
2	2.1	Develop the Architecture	Create the technical architecture of the website.	System Architect	15/1/2024	19/1/2024
2	2.2	Develop Product Database	Build the database to store product information.	Database Administrator	20/1/2024	24/1/2024
2	2.3	Develop Web Site	Develop all website features and functionalities.	Web Developer	25/1/2024	31/1/2024
2	2.4	Test the Site	Test the website to ensure it meets requirements.	QA Tester	1/2/2024	4/2/2024
2	3.1	Perform Risk Management	Identify and mitigate potential project risks.	Risk Manager	5/2/2024	9/2/2024
2	3.2	Perform Quality Assurance	Ensure project meets quality standards.	QA Manager	10/2/2024	14/2/2024
2	3.3	Perform Issue Management	Track and resolve project issues.	Project Manager	15/2/2024	19/2/2024
2	4.1	Perform Deployment	Launch the website and ensure functionality.	Deployment Team	20/2/2024	25/2/2024

Note: the WBS does not dictate the order in which these tasks must be executed. To understand the sequence, we need to refer to our project schedule

SWINBURNE UNIVERSITY OF TECHNOLOGY

05 - Validate Scope (A1)

Process of Acceptance:

- Formal acceptance of completed deliverables by stakeholders.

Verification Techniques:

- Inspections, reviews, audits, walkthroughs

Inputs:

- Project Management Plan, verified deliverables, work performance data

Outputs

- Accepted deliverables, work performance information, change requests, project documents updates.


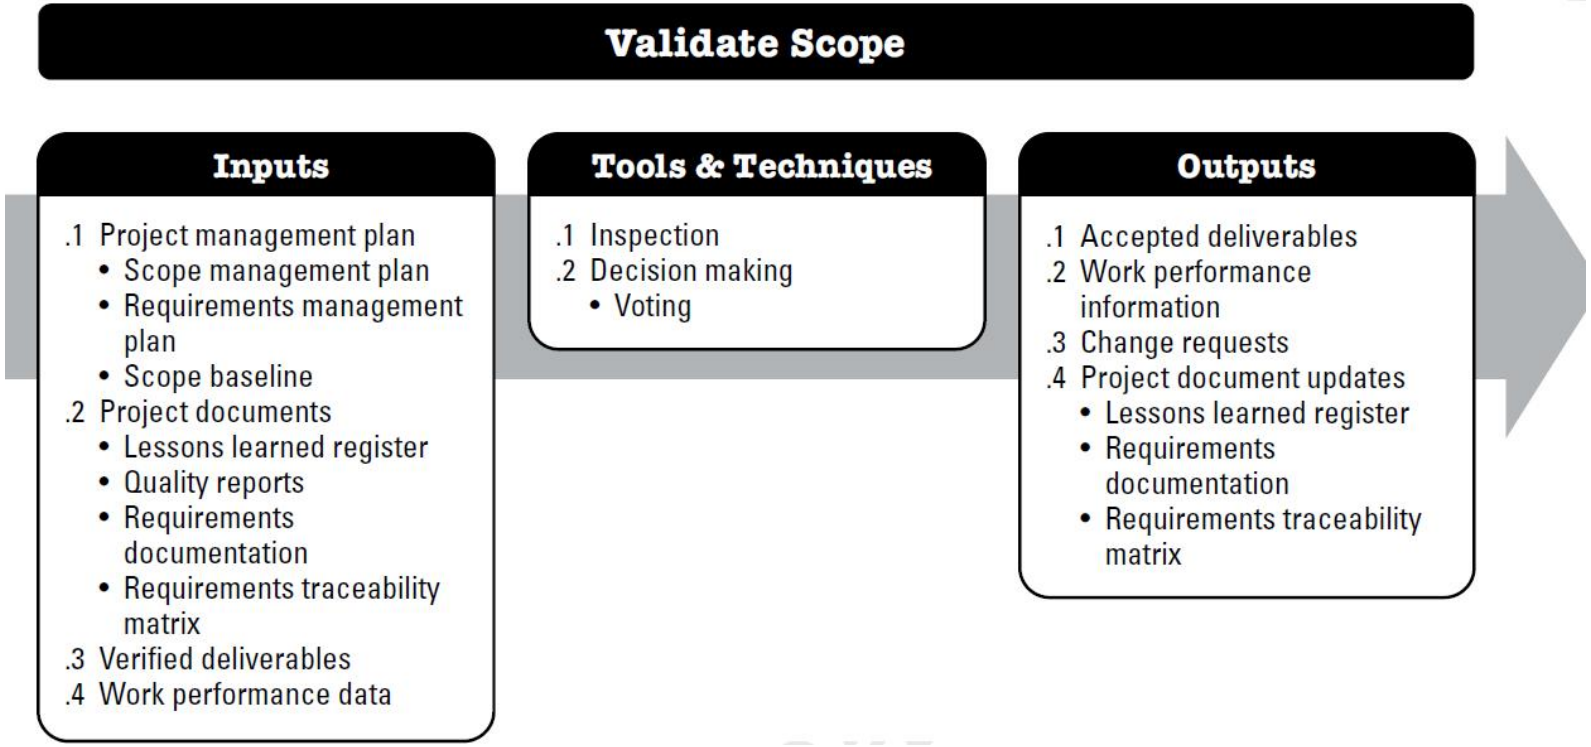


Image from [Project Scope Management on projectengineer.net]

06 - Control Scope (A1, week 3)

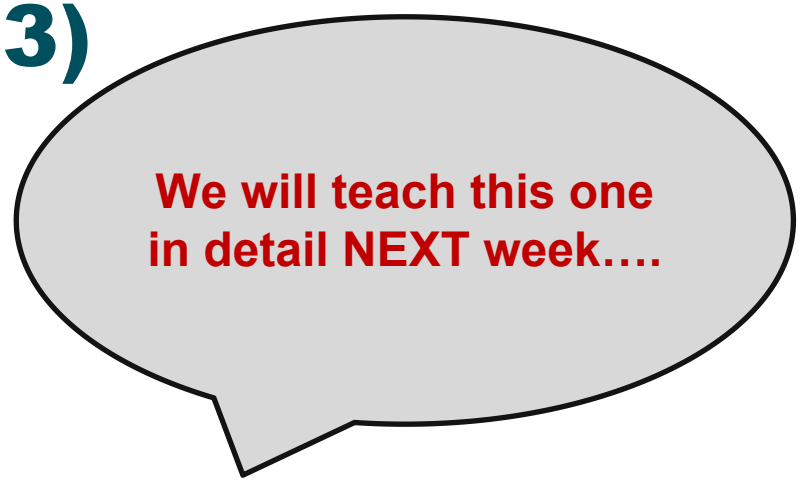

Managing Changes to Scope:

- Identify scope changes, evaluate impact, approve/reject changes.

Importance of Monitoring and Control:

- Ensures the project stays on track and meets its objectives.
- Helps in managing scope creep and ensuring only approved changes are implemented.

Tools & Techniques

- Variance analysis, trend analysis, change control tools.

Outputs

- Work performance information, change requests, project management plan updates, project documents updates.

SWINBURNE UNIVERSITY OF TECHNOLOGY

Time Management



Image Source: [Project Management Memes Visor Blog]

SWINBURNE UNIVERSITY OF TECHNOLOGY

Time Management - Definition



Image Source: [Bing]

Time Management:

Planning, estimating, scheduling, and controlling project activities to ensure timely completion of the project.

Key Components

- **Activity** : The process of identifying and documenting the specific actions to be performed to produce the project deliverables.
- **Sequencing**: Determining the order in which project activities will be performed.
- **Resource Estimation**: Estimating the type and quantities of resources required to perform each activity.
- **Duration Estimation**: Estimating the number of work periods needed to complete individual activities.
- **Schedule Development**: Analyzing activity sequences, durations, resource requirements, and schedule constraints to create the project schedule model.
- **Schedule Control**: Monitoring the status of project activities to update project progress and manage changes to the schedule baseline.

SWINBURNE UNIVERSITY OF TECHNOLOGY

Time Management Processes

Processes:

- **Plan Schedule Management**
  - Establishes policies, procedures, and documentation for planning, developing, managing, executing, and controlling the project schedule.
- **Define Activities**
  - Identifying and documenting the specific actions to be performed to produce the project deliverables.
- **Sequence Activities**
  - Identifying and documenting relationships among project activities.
- **Estimate Activity Resources & Durations**
  - Estimating the type and quantities of resources required to perform each activity and the number of work periods needed to complete individual activities.
- **Develop Schedule**
  - Analyzing activity sequences, durations, resource requirements, and schedule constraints to create the project schedule model.
- **Control Schedule**
  - Monitoring the status of project activities to update project progress and manage changes to the schedule baseline.

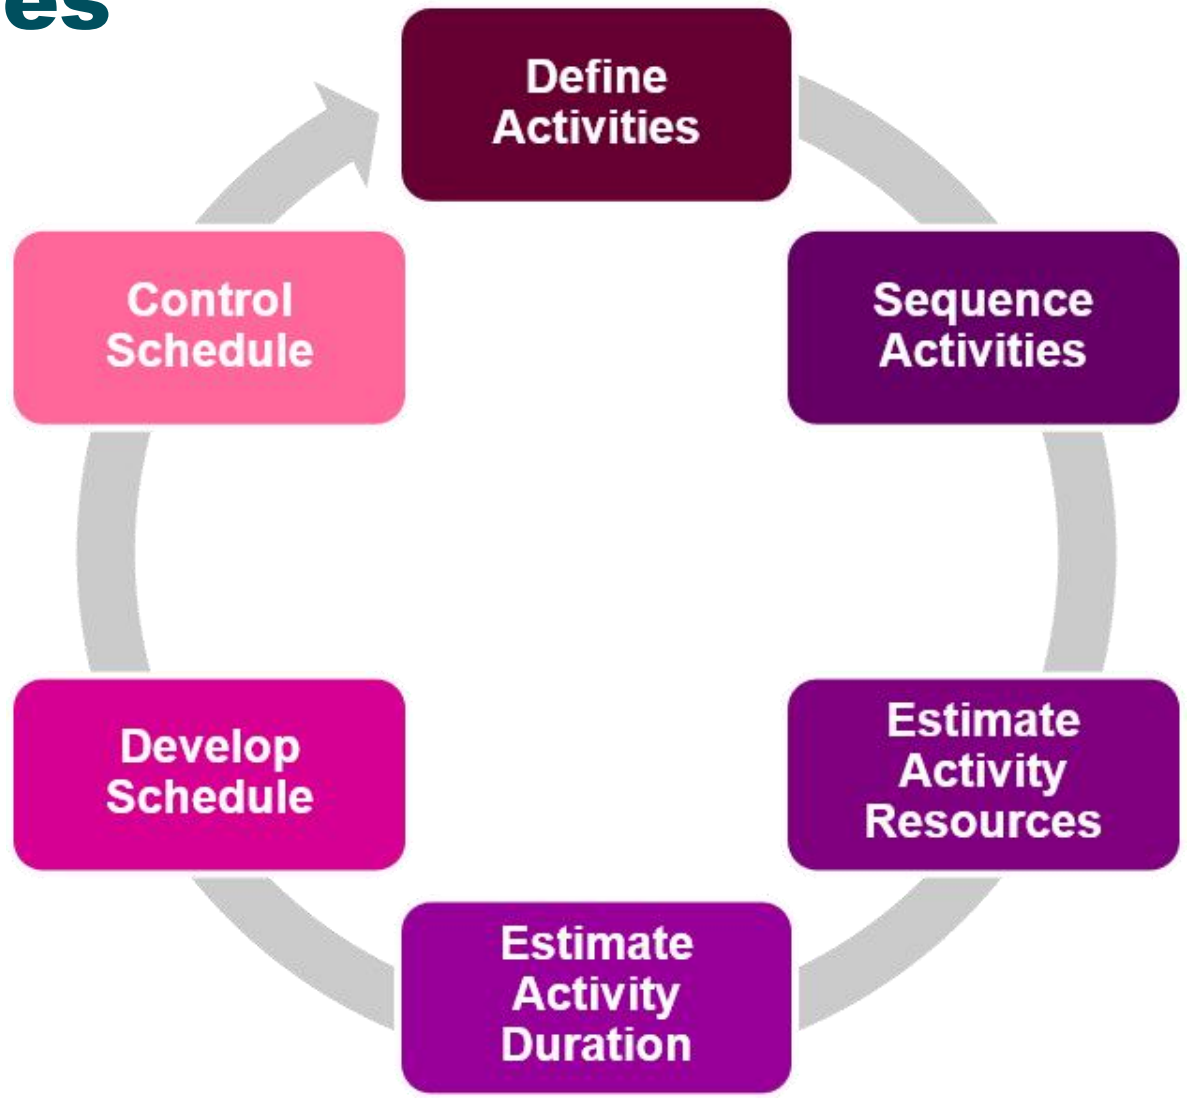


Image from [Project Time Management CUBES Project]

SWINBURNE UNIVERSITY OF TECHNOLOGY

01 - Plan Schedule Management

What's for?

Provides guidelines on how the project schedule will be managed, ensuring all activities are planned, developed, managed, executed, and controlled effectively.

> Inputs:

- Project charter, project management plan

> Tools & Techniques:

- Expert judgment, meetings

> Outputs:

- Schedule management plan



Image from [What is Time Management in Project Management on geeksforgeeks.org]

02- Define Activities

Definition:

The process of identifying and documenting the specific actions to be performed to produce the project deliverables.

- **Breaking Down Work Packages**: Activities are derived from work packages, which are the lowest level of the Work Breakdown Structure (WBS).
- **Activity List**: A comprehensive list of all activities required to complete the project.
- **Activity Attributes**: Detailed descriptions of each activity, including predecessor and successor activities, logical relationships, leads and lags, resource requirements, constraints, and assumptions.
- **Milestone List**: Significant points or events in the project timeline, such as the completion of major deliverables.

Importance of Defining Activities:


- **Clarity and Focus**: Clearly defined activities provide a detailed understanding of what needs to be done, ensuring that all team members are on the same page.
- **Baseline for Scheduling**: The activity list serves as the foundation for developing the project schedule, helping to allocate resources and estimate durations accurately.
- **Enhanced Monitoring and Control**: Detailed activity descriptions enable better tracking of project progress and facilitate effective control measures.

SWINBURNE UNIVERSITY OF TECHNOLOGY

03 - Sequence Activities

Definition:

The process of identifying and documenting relationships among project activities to define the logical sequence in which they will be performed.

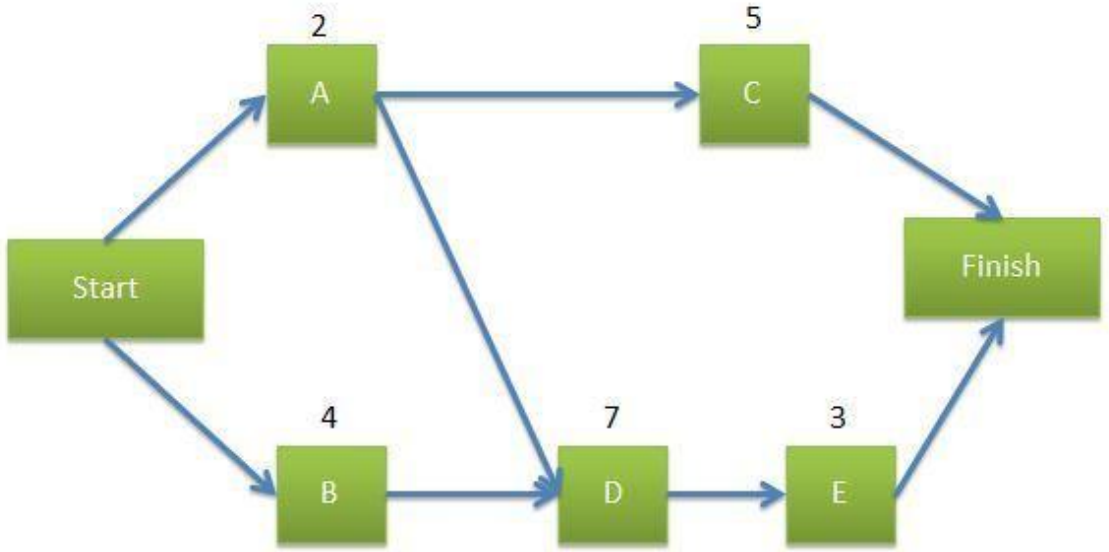

Importance:

Ensures that activities are performed in the correct order, considering dependencies and constraints. Allows project managers to focus on critical tasks that directly impact the project's completion date.

Tools & Techniques for Sequencing Activities:

- Network Diagrams: Visual representation of activity sequencing.
- Precedence Diagramming Method (PDM): Method to sequence activities using nodes and arrows.

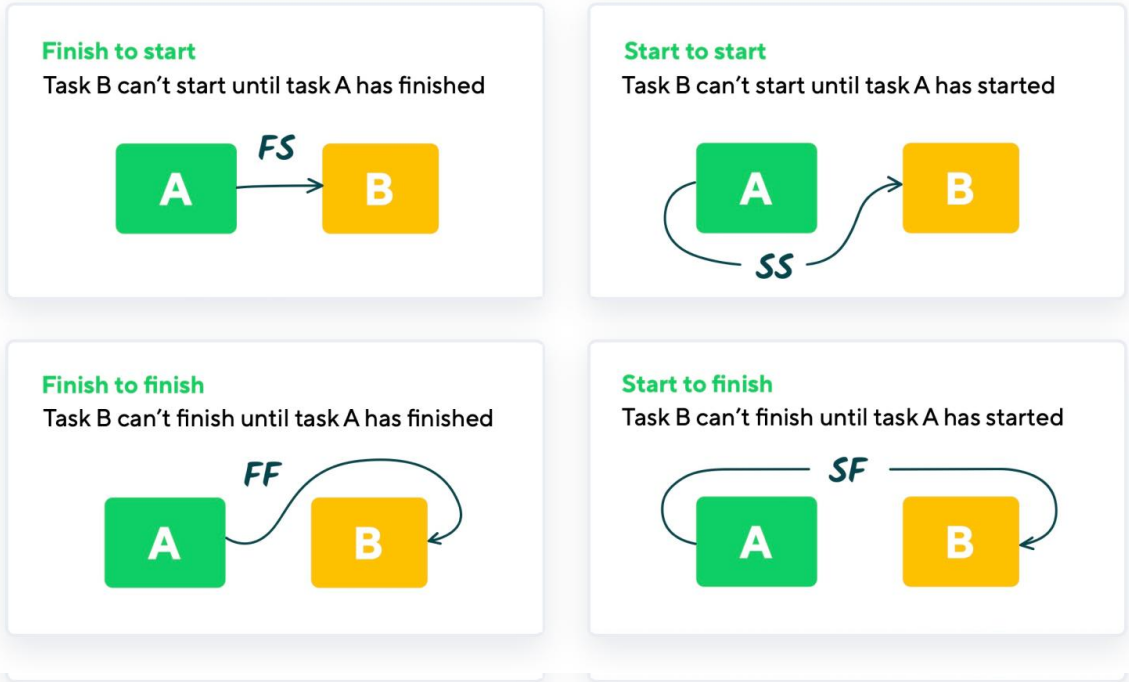


Image from [Network Diagram in Project Management Wrike Project Management Guide]

04 - Estimate Activity Resources & Durations

Definition

The process of estimating the type and quantities of resources required to perform each activity and the amount of time each activity will take to complete.

Estimation Techniques

- Expert Judgment: Using experts' experience to estimate activity durations.
- Analogous Estimating: Using historical data from similar projects.
- Parametric Estimating: Using statistical relationships between historical data and other variables.
- Three-Point Estimating: Using optimistic, pessimistic, and most likely estimates to calculate an average duration.
- Bottom-Up Estimating: Aggregating the estimates of lower-level components of the WBS.

Importance of Accurate Estimates

- Ensures realistic schedule and resource allocation.
- Helps in setting achievable deadlines and managing stakeholder expectations.

Outputs

- Activity duration estimates, basis of estimates, project documents updates.

SWIN BUR NE SWINBURNE UNIVERSITY OF TECHNOLOGY

05 - Develop Schedule (A1)

Definition:

- **Develop Schedule**: The process of analyzing activity sequences, durations, resource requirements, and schedule constraints to create the project schedule model. This process results in the project schedule, which serves as a baseline for monitoring and controlling project progress.

Tools:

- **Gantt Charts**: A bar chart that represents a project schedule showing the start and finish dates of the project elements.
- **Critical Path Method (CPM):** A schedule network analysis technique used to determine the amount of scheduling flexibility (the amount of float) on various logical network paths in the project schedule network, and to determine the minimum total project duration.
- **PERT (Program Evaluation and Review Technique):** A statistical tool used to analyze and represent the tasks involved in completing a given project, which is used especially in the context of time required to complete each task, and to identify the minimum time needed to complete the total project.

Importance:

- Helps in ensuring that the project is completed on time
- Helps in effective allocation and management of resources
- Provides a baseline for tracking project progress and identifying any delays or issues early.

SWINBURNE UNIVERSITY OF TECHNOLOGY

Developing A Gantt Chart

Step 1: Review Scope Baseline

- Understand project objectives and deliverables.
- Identify major milestones and phases.
- Review constraints and assumptions.

Step 2: Create Activities

- Break down project work into tasks.
- Ensure tasks are clearly defined.
- Use Work Breakdown Structure (WBS).

Step 3: Sequence Activities

- Determine the order of tasks.
- Identify dependencies.
- Use network or precedence diagrams.

Step 4: Estimate Resources

- Determine type and quantity of resources for each task.
- Consider human resources, equipment, and materials.
- Allocate resources based on availability.

Step 5:Estimate Durations

- Estimate the time required for each task.
- Use historical data or expert judgment.
- Consider risks and uncertainties.

Step 6:Develop Schedule

- Compile sequences, durations, and resources into a schedule.
- Use Gantt chart software for visualization.
- Adjust the schedule as needed.

SWINBURNE UNIVERSITY OF TECHNOLOGY

05 - Develop Schedule - Gantt Chart (Example)

Definition


- A visual tool to represent the project schedule.

Purpose

- To help track planned progress against actual progress

Key features:

- tasks with ID
- width of the bar (duration/time intervals)
- directional arrow (sequence/dependence)
- different colors (phase)
- some tasks can be conducted individually, not dependent to prior tasks (e.g. tasks in Monitoring and Control)
- some tasks may happen simultaneously (e.g. 1.2 and 1.3)

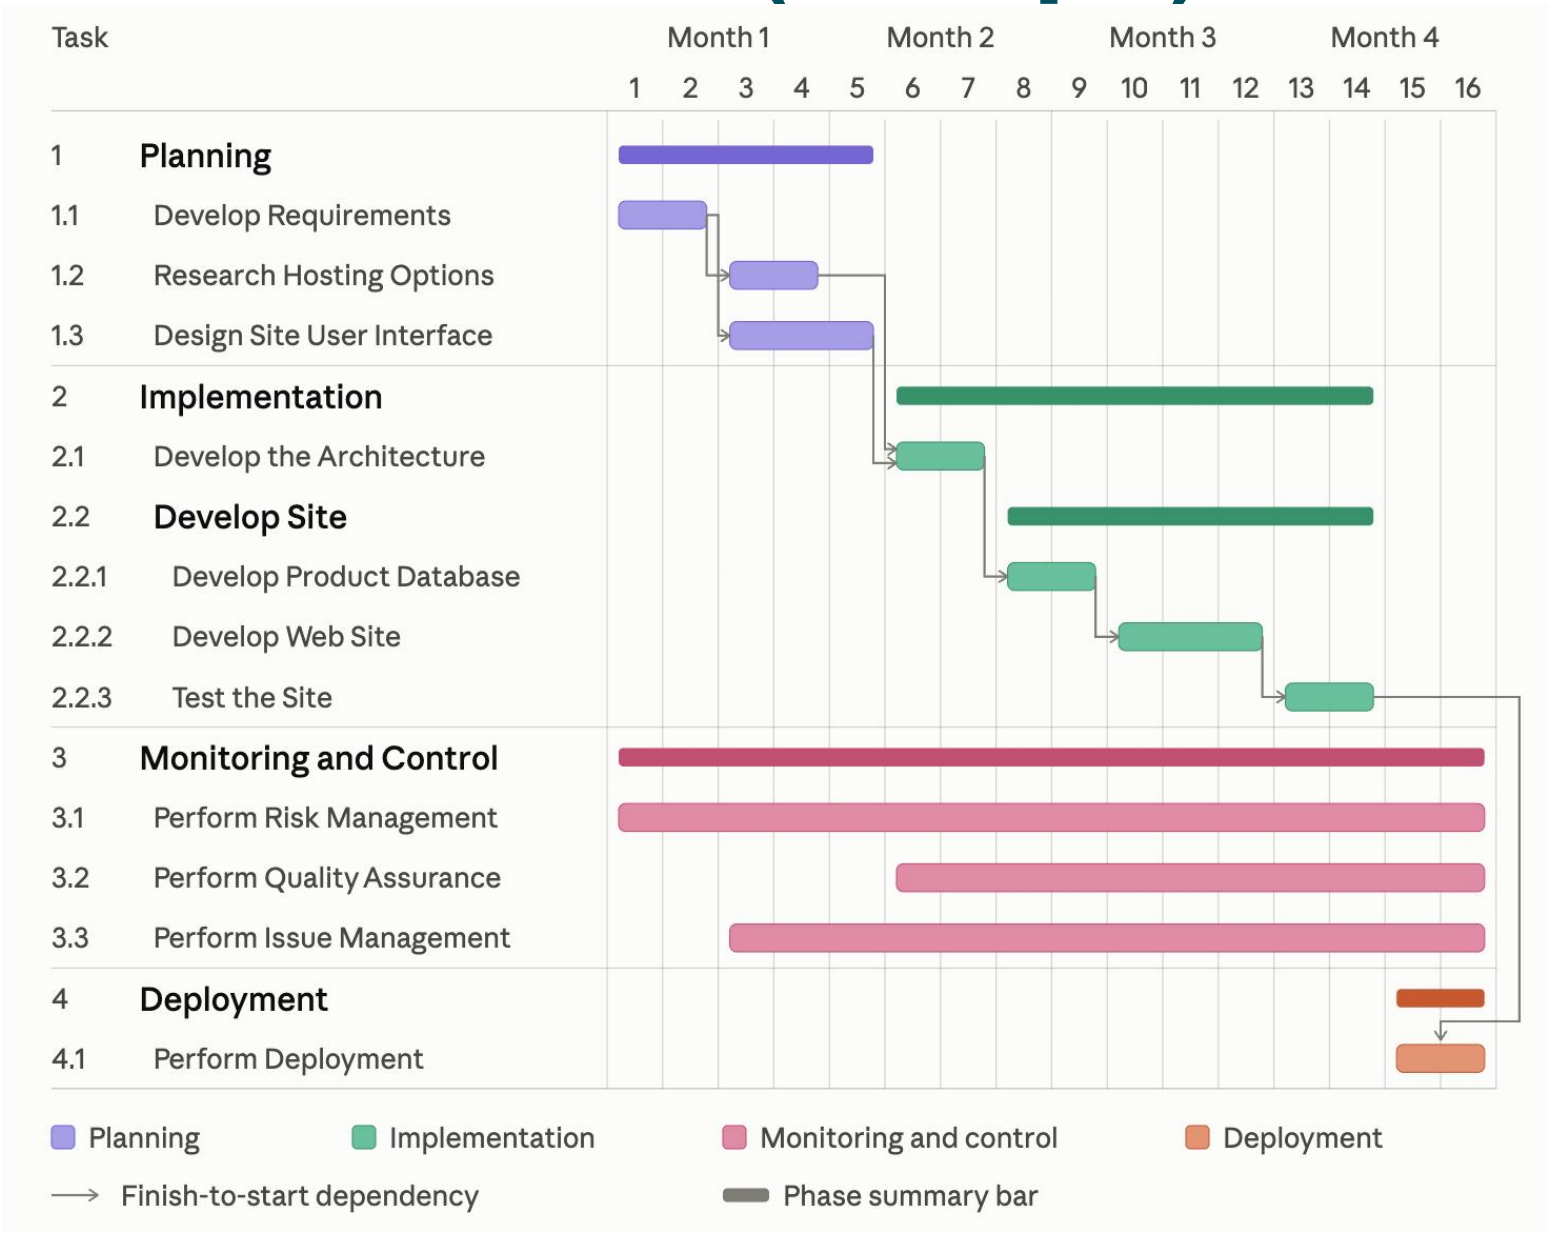

05 - Develop Schedule - Critical Path Method

Definition:

CPM: A project management technique that determines the sequence of activities that directly affect the project completion time. It identifies the longest path through the project, known as the critical path, and helps in determining the shortest possible project duration.


Purpose:

Helps in identifying tasks that cannot be delayed without affecting the project's completion date.

Steps to Apply Critical Path Method:

1. List All Activities: Identify and list all project activities.
2. Determine Dependencies: Define the dependencies between activities.
3. Estimate Duration: Estimate the time required to complete each activity.
4. Construct Network Diagram: Create a network diagram showing the sequence of activities.
5. Calculate Critical Path: Determine the longest path through the network diagram to identify the critical path.
6. Monitor and Adjust: Continuously monitor the critical path and make adjustments as necessary to keep the project on track.

In order to determine the critical path, network diagram of the project is drawn:

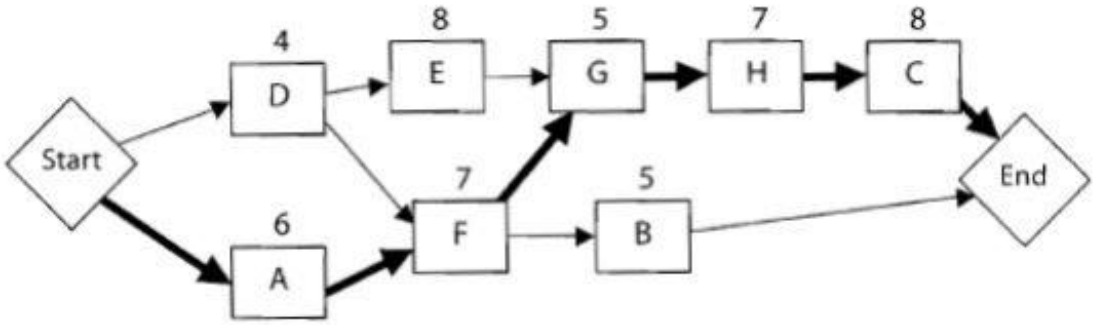

We see that this project has 5 paths and the duration of the critical path is 33 months. As a result the duration of the project is also 33 months. (Mulcahy, 2005)

Paths	Duration
Start, D, E, G, H, C, End	32
Start, D, F, G, H, C, End	31
Start, D, F, B, End	16
Start, A, F, G, H, C, End	33
Start, A, F, B, End	18

Image Source: by [Mastering the Basics of Project Management: The Critical Path Method (CPM) Nelson B.J. Blog]

06 - Schedule Control

Monitoring Progress:

- Regularly tracking, reviewing, and regulating the progress of project activities.

Schedule Variance and Performance Index:

- Measure performance using metrics like Schedule Variance (SV) and Schedule Performance Index (SPI).

Definitions:

- **Schedule Variance (SV)**: A measure of schedule performance expressed as the difference between the earned value (EV) and the planned value (PV).
- **Schedule Performance Index (SPI)**: A measure of schedule efficiency expressed as the ratio of earned value (EV) to planned value (PV).

Note: SV and SPI will be explained further in **week 3**

SWINBURNE UNIVERSITY OF TECHNOLOGY

PROJECT COMMUNICATIONS MANAGEMENT



Image Source: [Project Management Memes Visor Blog]

SWINBURNE UNIVERSITY OF TECHNOLOGY

Project Communication Management (A1)

Overview

Project Communications Management involves the processes required to ensure timely and appropriate planning, collection, creation, distribution, storage, retrieval, management, control, monitoring, and the ultimate disposition of project information. Effective communication is critical for successful project management as it ensures that information is properly disseminated among project stakeholders.

Impact on Project Success

- Ensures that all stakeholders are informed and involved.
- Facilitates coordination and collaboration among project team members.
- Helps in managing stakeholder expectations and resolving conflicts.

Key Components

- Planning Communications Management: Determining the information and communications needs of the stakeholders.
- **Managing Communications**: Creating, collecting, distributing, storing, retrieving, and disposing of project information.
  - **Includes Minutes of Meetings**: Documenting discussions, decisions, and action items from meetings.
- Monitoring Communications: Ensuring the information needs of the project and its stakeholders are met.

SWINBURNE UNIVERSITY OF TECHNOLOGY

Planning Communications Management (A1)

Purpose

- To develop an appropriate approach and plan for project communications based on stakeholder's information needs and requirements, and available organizational assets.

Inputs

- Project charter, project management plan, stakeholder register, enterprise environmental factors, organizational process assets.

Tools & Techniques

- Expert judgment, communication requirements analysis, communication technology, communication models, communication methods, meetings.

Outputs

- Communications management plan, project documents updates.

SWIN BUR NE
SWINBURNE UNIVERSITY OF TECHNOLOGY

Managing Communications

Purpose

- Ensures timely and appropriate collection, creation, distribution, storage, retrieval, management, monitoring, and the ultimate disposition of project information.

Steps

- Identify the information needs of stakeholders.
- Determine the best way to meet those needs.
- Implement the communications plan.
- Monitor and adjust communications as needed.

Tools & Techniques

- Communication technology, communication models, communication methods, information management systems, performance reporting.

Outputs

- Project communications, project management plan updates, project documents updates, organizational process assets updates.

SWIN BUR NE SWINBURNE UNIVERSITY OF TECHNOLOGY

Managing Communications - Minutes of Meeting (A1)

Definition:

- Minutes of meeting are the written record of everything that happened during a meeting.

Purpose

- To provide a formal, structured documentation of discussions, decisions, and actions.
- Ensures accountability and follow-up on action items.
- Serves as a reference for future meetings.



Benefits

- Captures key points and decisions,. This helps in maintaining a clear and comprehensive record of the meeting.
- Ensures accountability and follow-up on action items, it ensures that team members are accountable for their tasks.
- Serves as a reference for future meetings, provide a historical record that helps in understanding the context of previous discussions, tracking progress, and making informed decisions.

SWINBURNE UNIVERSITY OF TECHNOLOGY

Monitoring Communications

Purpose

- Ensures that stakeholder communication needs are being met and that communications are effective.

Steps

- Monitor communication activities.
- Evaluate the effectiveness of communication efforts.
- Make adjustments as needed.

Tools & Techniques

- Information management systems, expert judgment, meetings.

Outputs

- Work performance information, change requests, project management plan updates, project documents updates.

SWINBURNE UNIVERSITY OF TECHNOLOGY

COS30049 – Computing Technology Innovation Project

Week 2 - Scope, Time, and Project Communication Management


(Lecture – 02)

Ningran Li (Icey)
ningranli@swin.edu.au

Developing A Meeting Minutes

What are Meeting Minutes?

- **Definition**: Meeting minutes are the written record of everything that happened during a meeting.
- **Purpose**: To provide a formal, structured documentation of discussions, decisions, and actions.
- **Benefits**:
  - Capture key points and decisions.
  - Ensure accountability and follow-up on action items.
  - Serve as a reference for future meetings.

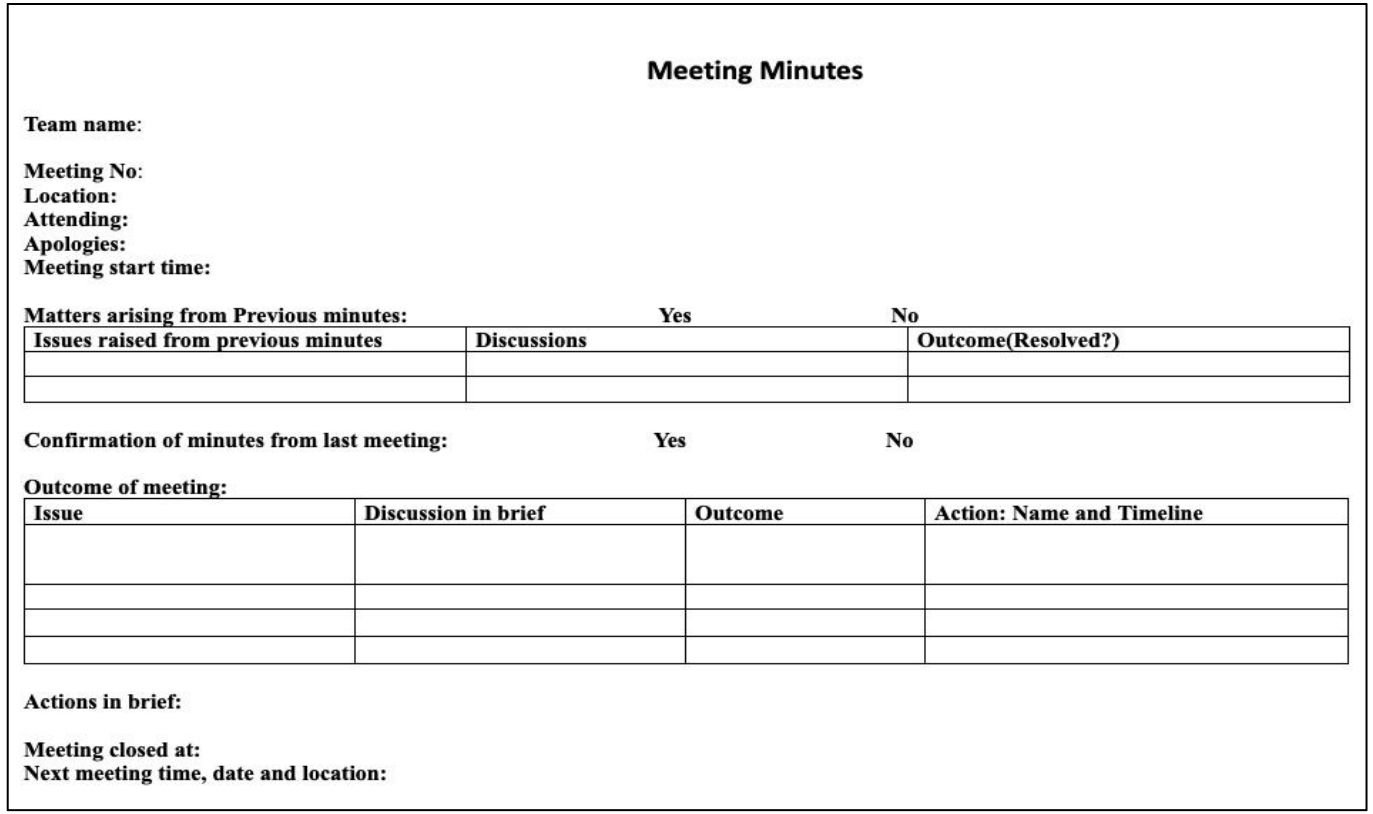

Meeting Minutes

Team name:

Meeting No:
Location:
Attending:
Apologies:
Meeting start time:

Matters arising from Previous minutes: **Yes** **No**

Issues raised from previous minutes	Discussions	Outcome(Resolved?)

Confirmation of minutes from last meeting: **Yes** **No**

Outcome of meeting:

Issue	Discussion in brief	Outcome	Action: Name and Timeline

Actions in brief:

Meeting closed at:
Next meeting time, date and location:

SWINBURNE UNIVERSITY OF TECHNOLOGY

Developing A Meeting Minutes – Steps

1. **Prepare for the Meeting**:

Review the agenda and understand the objectives: Make sure you know what topics will be covered and what outcomes are expected.

- **Gather necessary materials and templates**: Have all the documents and tools you need ready before the meeting starts.

2. Take Notes During the Meeting:

- Record attendees, time, and date.
- Capture key discussions, decisions, and assigned tasks.

3. Write the Minutes:

- Use a clear and concise format.
- Include essential details such as agenda items, discussions, decisions, and action items.

4. Review and Distribute:

- Review for accuracy and completeness.
- Distribute to attendees and relevant stakeholders.

SWINBURNE UNIVERSITY OF TECHNOLOGY

Any Questions?



Image Source: [Project Management Memes Visor Blog]
